



Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56
11.19.2023 – 11.25.2023

SKANSKA

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56

Construction Progress

<i>General / Misc.</i>	<ul style="list-style-type: none">• FRP column set front porch• Upper trim work front porch• Toilet accessory installation• Patch work on FRP columns• Cornice work at front porch and Plumb Alley
<i>Mechanical</i>	<ul style="list-style-type: none">• Fourth floor ceiling grid rough-in• Insulation for duct third floor• Duct labeling fourth floor• Refrigerant line installation third floor
<i>Electrical</i>	<ul style="list-style-type: none">• Fourth floor detention light rough-in• Fourth floor hallway lighting• Third floor fire alarm conduit• Third floor power conduit and pulling wire• Installing can lights in third floor drop ceilings• Security conduit third floor
<i>Walls/Framing</i>	<ul style="list-style-type: none">• Framing for cornice Plumb Alley side• Hanging ballistic panels main entrance• Drywall touch-up third floor• Hanging drywall and finishing at main entrance• Cutting in borders for fourth floor ceiling grid
<i>Other</i>	<ul style="list-style-type: none">• Elevator 3 installation• Hard tile installation fourth floor toilets• Security wire pull third floor detention area• Site layout and receipt of detention product

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56

Safety and Quality Assurance

- No safety incidents to report this week.
- Skanska continues to observe and document work in progress.

Schedule

- New Addition is scheduled to be complete by spring 2024.
- Renovations are scheduled to be complete by January 2025.

Meetings

- Meetings held:
 - Construction Progress Meeting: 11/22/2023 @ 11 AM
- Upcoming:
 - Construction Progress Meeting: 12/06/2023 @ 11 AM

Project Administration

- Construction Contract:
 - Original contract value (GMP): \$27,885,975.00
 - Net value of change orders to-date: (\$5,116,901.47)
 - Current contract value: \$22,769,073.53
- Owner Direct Purchase Process:
 - Total value of purchase orders issued to-date: \$4,827,107.80
 - Tax savings to-date: \$255,367.32

Progress Photos – see next page

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56



Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56




Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56



Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56

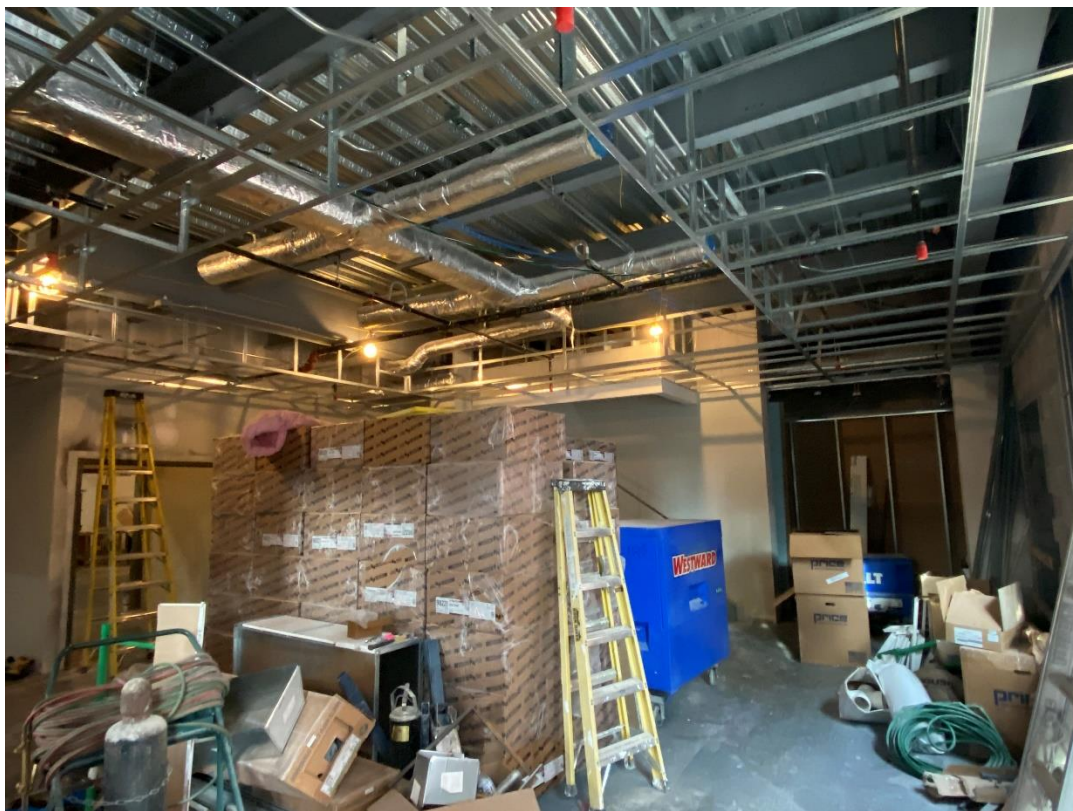

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #56

