



Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63
01.07.2024 – 01.13.2024

SKANSKA

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63

Construction Progress

<i>General / Misc.</i>	<ul style="list-style-type: none">• Wood door hardware installation fourth floor• Exterior handrails at ramp• Painted trim installed in courtrooms third floor• Replacing ceiling tile fourth floor• Exterior door set at exit• PVC trim at exit door• Sidewalk demolition and grading/prep work
<i>Plumbing</i>	<ul style="list-style-type: none">• Water line vault work• Third floor detention fixtures
<i>Mechanical</i>	<ul style="list-style-type: none">• Third floor grilles and ceiling lay-in• Insulation for duct and plumbing
<i>Electrical</i>	<ul style="list-style-type: none">• Security conduit sally port area• Ceiling lay-in third floor
<i>Walls/Framing</i>	<ul style="list-style-type: none">• Drywall finish porch area ceiling• Ceiling tile borders third floor• Sanding drywall ramp area fourth floor
<i>Other</i>	<ul style="list-style-type: none">• Painting fourth floor walls and trim• Window frame installation fourth floor• Sprinkler head trim-out third and fourth floors• Elevator 3 installation• Security device installation third and fourth floors

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63

Safety and Quality Assurance

- No safety incidents to report this week.
- Skanska continues to observe and document work in progress.

Schedule

- New Addition is scheduled to be complete by spring 2024.
- Renovations are scheduled to be complete by January 2025.

Meetings

- Meetings held:
 - Construction Progress Meeting: 1/10/2024 @ 11 AM
- Upcoming:
 - Construction Progress Meeting: 1/24/2024 @ 11 AM

Project Administration

- Construction Contract:
 - Original contract value (GMP): \$27,885,975.00
 - Net value of change orders to-date: (\$5,116,901.47)
 - Current contract value: \$22,769,073.53
- Owner Direct Purchase Process:
 - Total value of purchase orders issued to-date: \$4,827,107.80
 - Tax savings to-date: \$255,367.32

Progress Photos – see next page


Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63




Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63

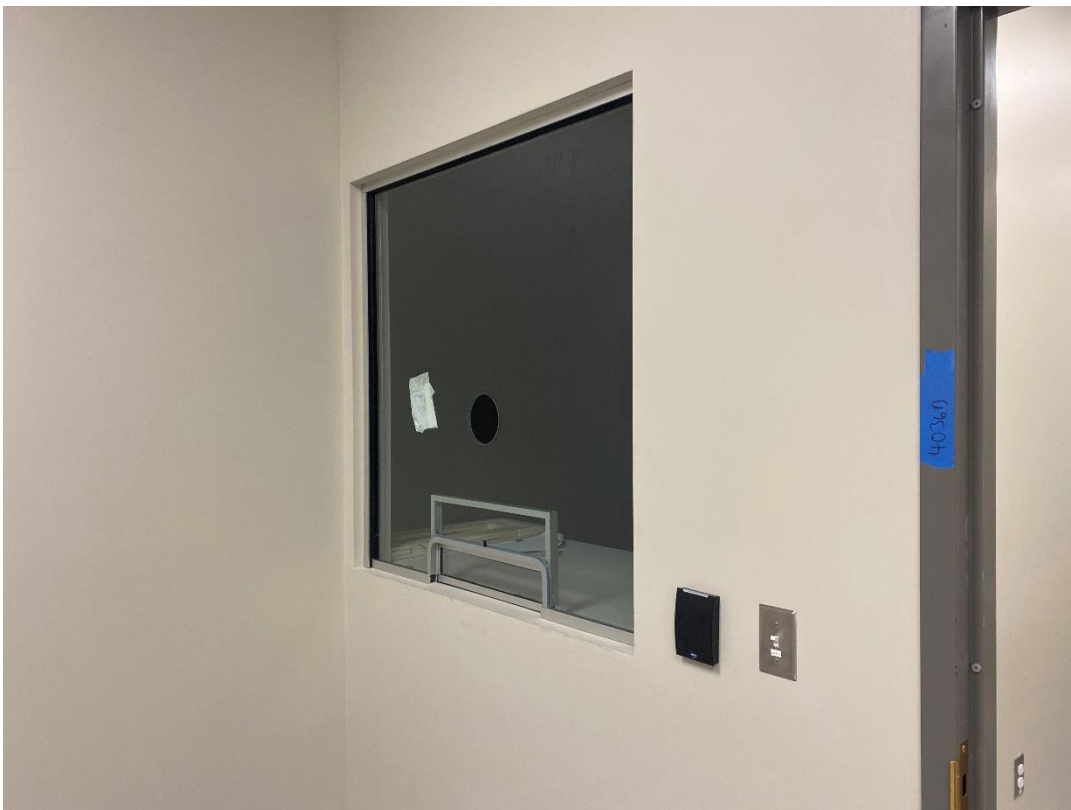

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63

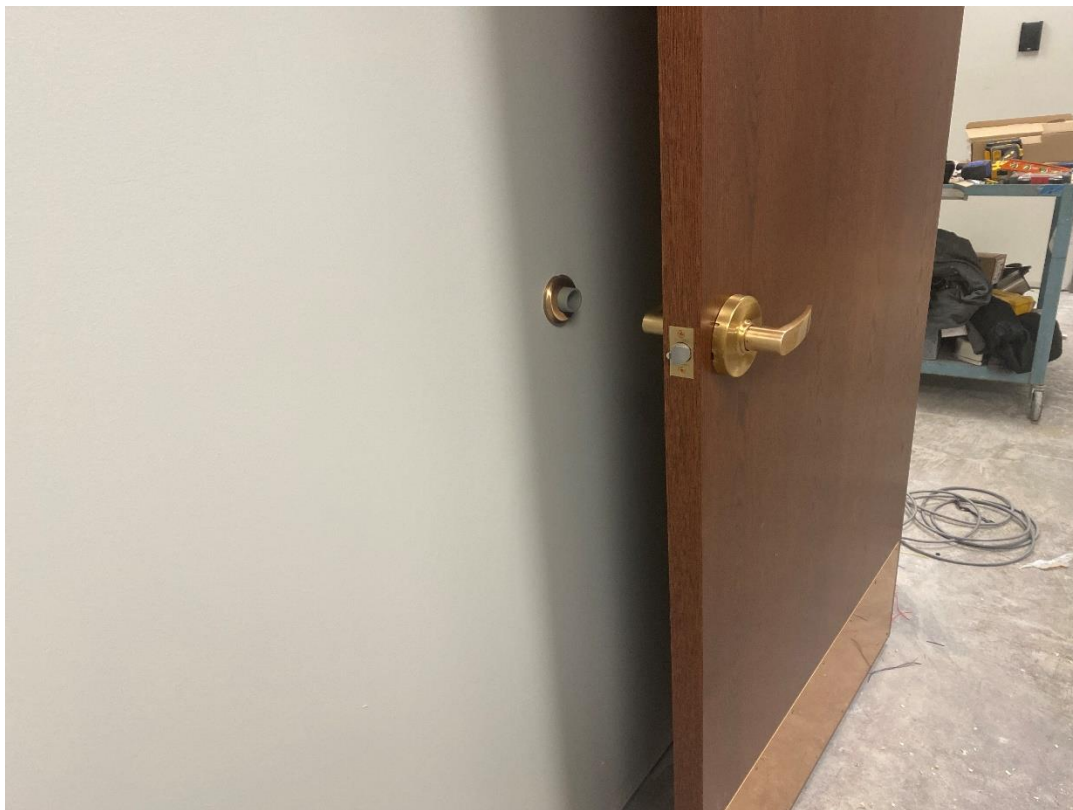

Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63



Washington County Courthouse Expansion & Renovation

Weekly Progress Report #63

