



# Washington County Courthouse Expansion & Renovation

Weekly Progress Report #67  
02.25.2024 – 03.02.2024

**SKANSKA**

# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67

### Construction Progress

<i>General / Misc.</i>	<ul style="list-style-type: none"><li>• Installing millwork in fourth floor J&amp;DR courtrooms</li><li>• Site clean up and miscellaneous punch list work</li></ul>
<i>Plumbing</i>	
<i>Mechanical</i>	<ul style="list-style-type: none"><li>• Testing and balancing HVAC system</li><li>• Punch list</li></ul>
<i>Electrical</i>	<ul style="list-style-type: none"><li>• Installing new feeder lines from new panel to existing Courthouse</li></ul>
<i>Walls/Framing</i>	
<i>Other</i>	<ul style="list-style-type: none"><li>• Painting in Judges' parking area and punch list</li><li>• Installing furniture</li><li>• Shades installed at windows</li><li>• Landscaping installed</li></ul>

# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67

### Safety and Quality Assurance

- No safety incidents to report this week.
- Skanska continues to observe and document work in progress, including completion of punch list items.

### Schedule

- Move-in date for the new addition is set for late March 2024.
- Renovations are scheduled to be complete by January 2025.

### Meetings

- Meetings held:
  - Courthouse Punchlist Walk-Through: 2/28/2024 @ 2 PM
- Upcoming:
  - Construction Progress Meeting: 3/6/2024 @ 11 AM

### Project Administration

- Construction Contract:
  - Original contract value (GMP): \$27,885,975.00
  - Net value of change orders to-date: (\$5,348,364.97)
  - Current contract value: \$22,537,610.03
- Owner Direct Purchase Process:
  - Total value of purchase orders issued to-date: \$5,047,762.16
  - Tax savings to-date: \$267,077.52

### Progress Photos – see next page



# Washington County Courthouse Expansion & Renovation


## Weekly Progress Report #67





# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67

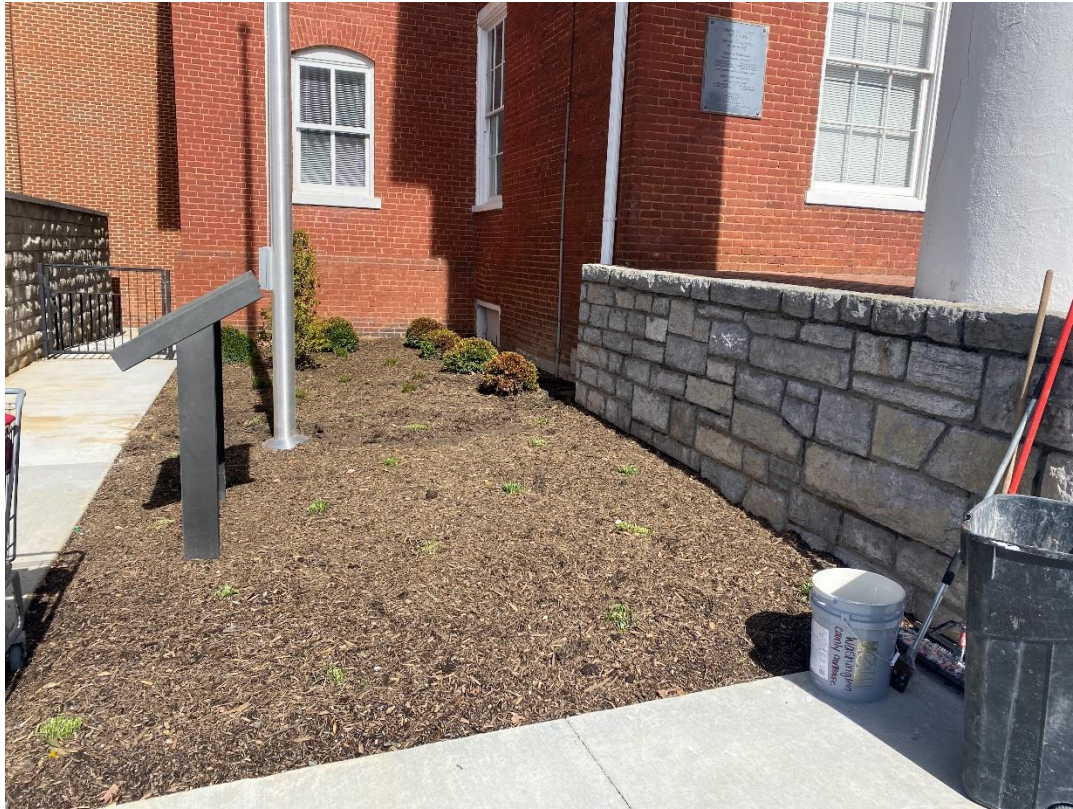



# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67



# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67





# Washington County Courthouse Expansion & Renovation

## Weekly Progress Report #67

